

The background of the slide is a photograph of a construction site at sunset. A large concrete pump truck with a long, articulated boom is silhouetted against the bright, low sun. The boom is extended high into the air, forming a wide 'V' shape. In the background, there are several large, dark, rectangular buildings under construction. A few construction workers in orange safety vests are visible near the base of the buildings. The sky is a mix of orange, yellow, and grey.

# BOND CONSTRUCTION UPDATE

# COMPLETED YEAR ONE PROJECTS

- RESTROOM RENOVATIONS AT 8 CAMPUSES
- WALL FINISHES AT 3 CAMPUSES
- THE COLONY HS ATHLETIC AREA RENOVATIONS
- VALLEY RIDGE ES PLAYGROUND REPLACEMENT
- STAGE CURTAINS AND LIGHTING REPLACEMENTS AT 7 CAMPUSES
- MARCUS HS TRACK AND TURF REPLACEMENT
- DONALD ES AND POLSER ES STEM ACADEMY RENOVATIONS





# ON-GOING YEAR ONE PROJECTS


- NEW CAREER CENTER WEST
- NEW MILL STREET ELEMENTARY SCHOOL
- POLSER ES 20-YEAR REFRESH
- CREEKSIDE ES 20-YEAR REFRESH
- DISTRICT WIDE ACCESS CONTROL UPGRADES
- EXTERIOR LIGHTING REPLACEMENTS – PHASE 1
- THE COLONY HS SOFTBALL FIELD REPLACEMENT
- MARCUS HS LIMITED REFRESH



# NEW CAREER CENTER





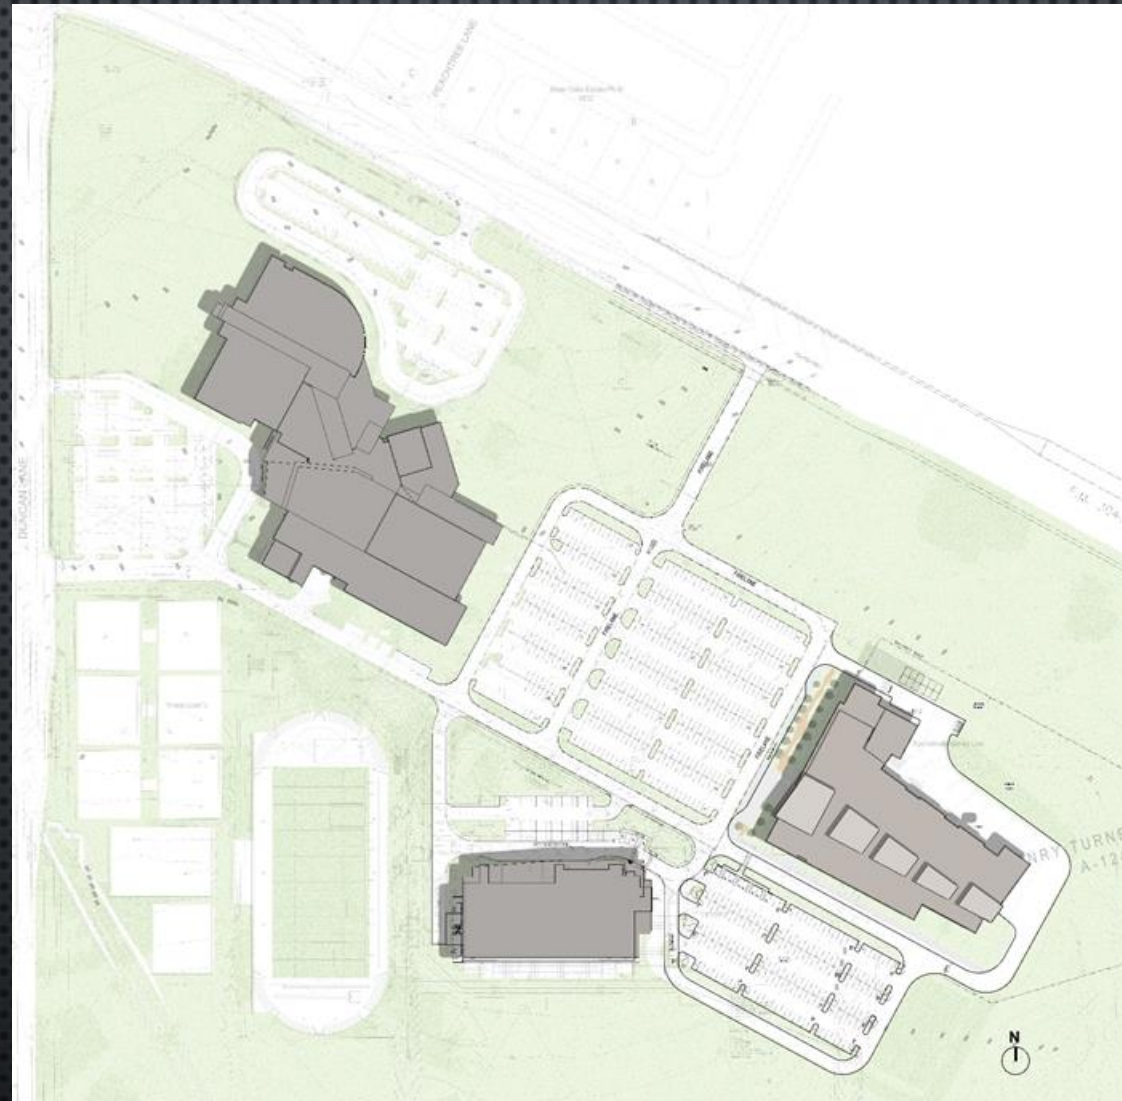

# NEW CAREER CENTER





NEW CAREER CENTER





NEW CAREER CENTER





NEW CAREER CENTER





NEW CAREER CENTER





NEW CAREER CENTER



# NEW MILL STREET ES







# NEW MILL STREET ES





NEW MILL STREET ES





NEW MILL STREET ES





NEW MILL STREET ES





NEW MILL STREET ES





NEW MILL STREET ES





NEW MILL STREET ES





**Balfour Beatty**  
Construction

*New Mill Street Elementary School*

Print #190131075  
Date: 01/31/19  
Lat/Lon: 33.040925 -96.994339  
Order No. 65536  
 Aerial Photography, Inc. 954-568-0484

# NEW MILL STREET ES





NEW MILL STREET ES



# TCHS SOFTBALL FIELD







THE COLONY HS SOFTBALL FIELD





THE COLONY HS SOFTBALL FIELD



# YEAR TWO PROJECTS

- NEW HEDRICK MIDDLE SCHOOL
- VICKERY TEN CLASSROOM ADDITION (STORM SHELTER)
- NEW JOSEY ELEMENTARY SCHOOL
- HEBRON HS MULTI-PURPOSE/IAC/PRACTICE FIELDS
- MIDDLE SCHOOL FINE ARTS ADDITIONS AND RENOVATIONS AT 3 CAMPUSES
- LISDOLA RENOVATIONS
- CENTRAL ES 20-YEAR REFRESH
- DEGAN ES 20-YEAR REFRESH
- PARKWAY ES 20-YEAR REFRESH
- TIMBERCREEK ES 20-YEAR REFRESH
- VALLEY RIDGE ES 20-YEAR REFRESH AND STEM ACADEMY





# YEAR TWO PROJECTS

- SECURITY VESTIBULE RENOVATIONS
- THE COLONY HS ENTRY RENOVATION
- THE COLONY HS LIMITED REFRESH
- EXTERIOR LIGHTING REPLACEMENTS — PHASE 2
- FOREST VISTA ES PLAYGROUND REPLACEMENT
- COLLEGE STREET RENOVATIONS
- CAMPUS SUPPORT RENOVATIONS
- LAKEVIEW MS FLOORING REPLACEMENT
- ETHRIDGE ES RE-ROOF
- FIBER AT 4 LOCATIONS






# NEW HEDRICK MS





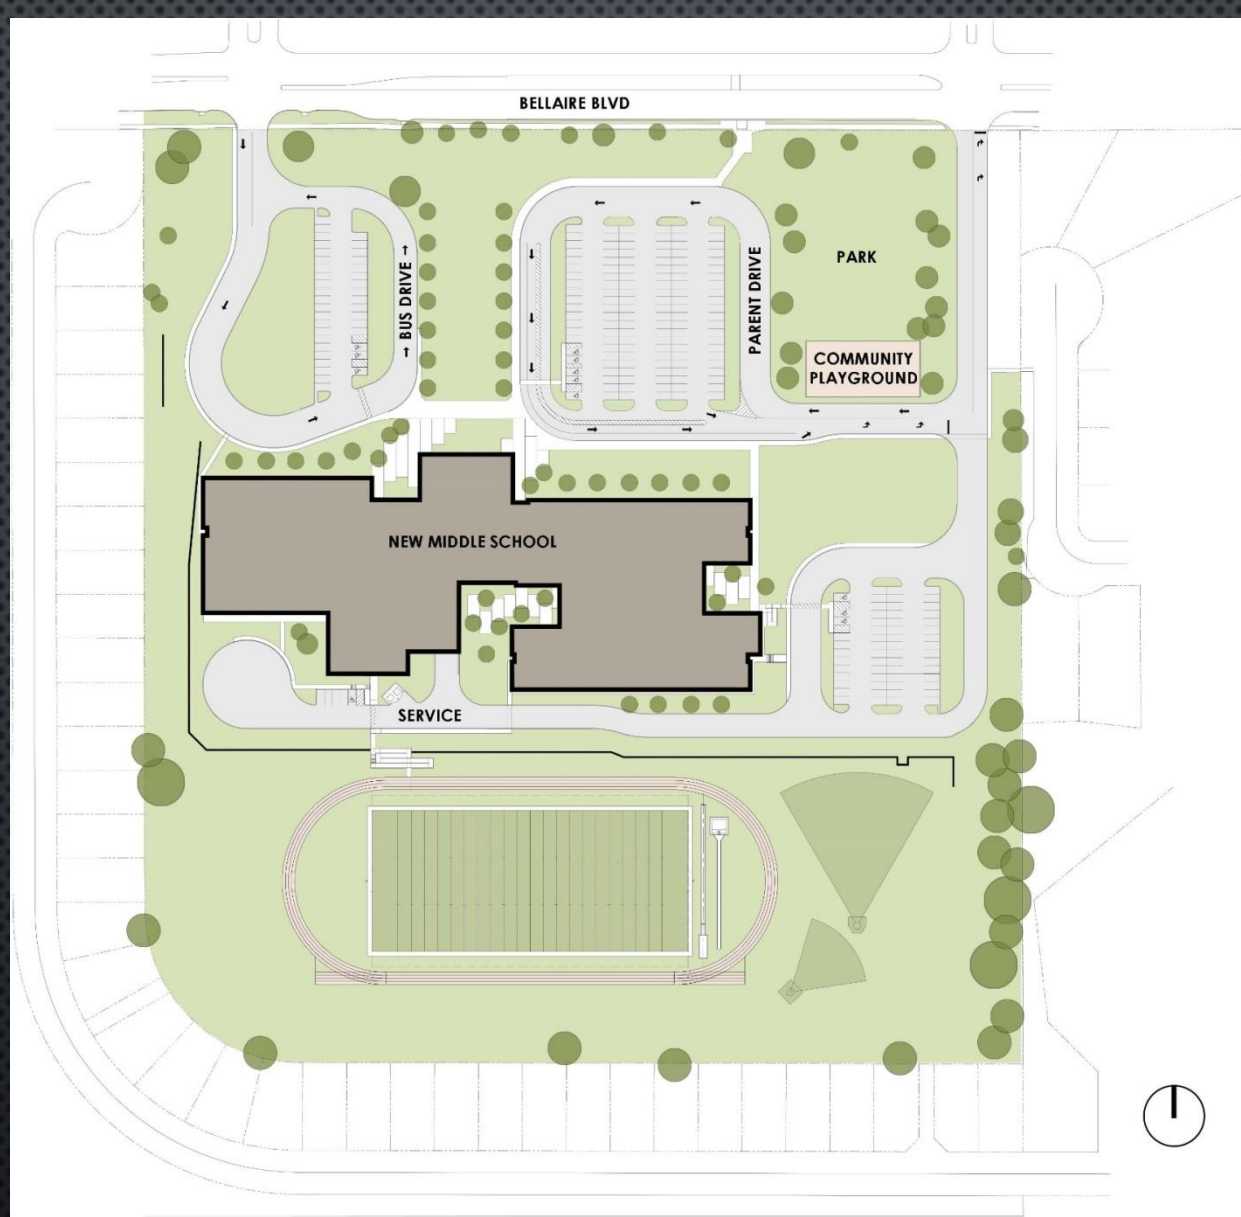

NEW HEDRICK MIDDLE SCHOOL





NEW HEDRICK MIDDLE SCHOOL





NEW HEDRICK MIDDLE SCHOOL





NEW HEDRICK MIDDLE SCHOOL





NEW HEDRICK MIDDLE SCHOOL





NEW HEDRICK MIDDLE SCHOOL






NEW HEDRICK MIDDLE SCHOOL



# HEBRON HS MULTI-PURPOSE/IAC





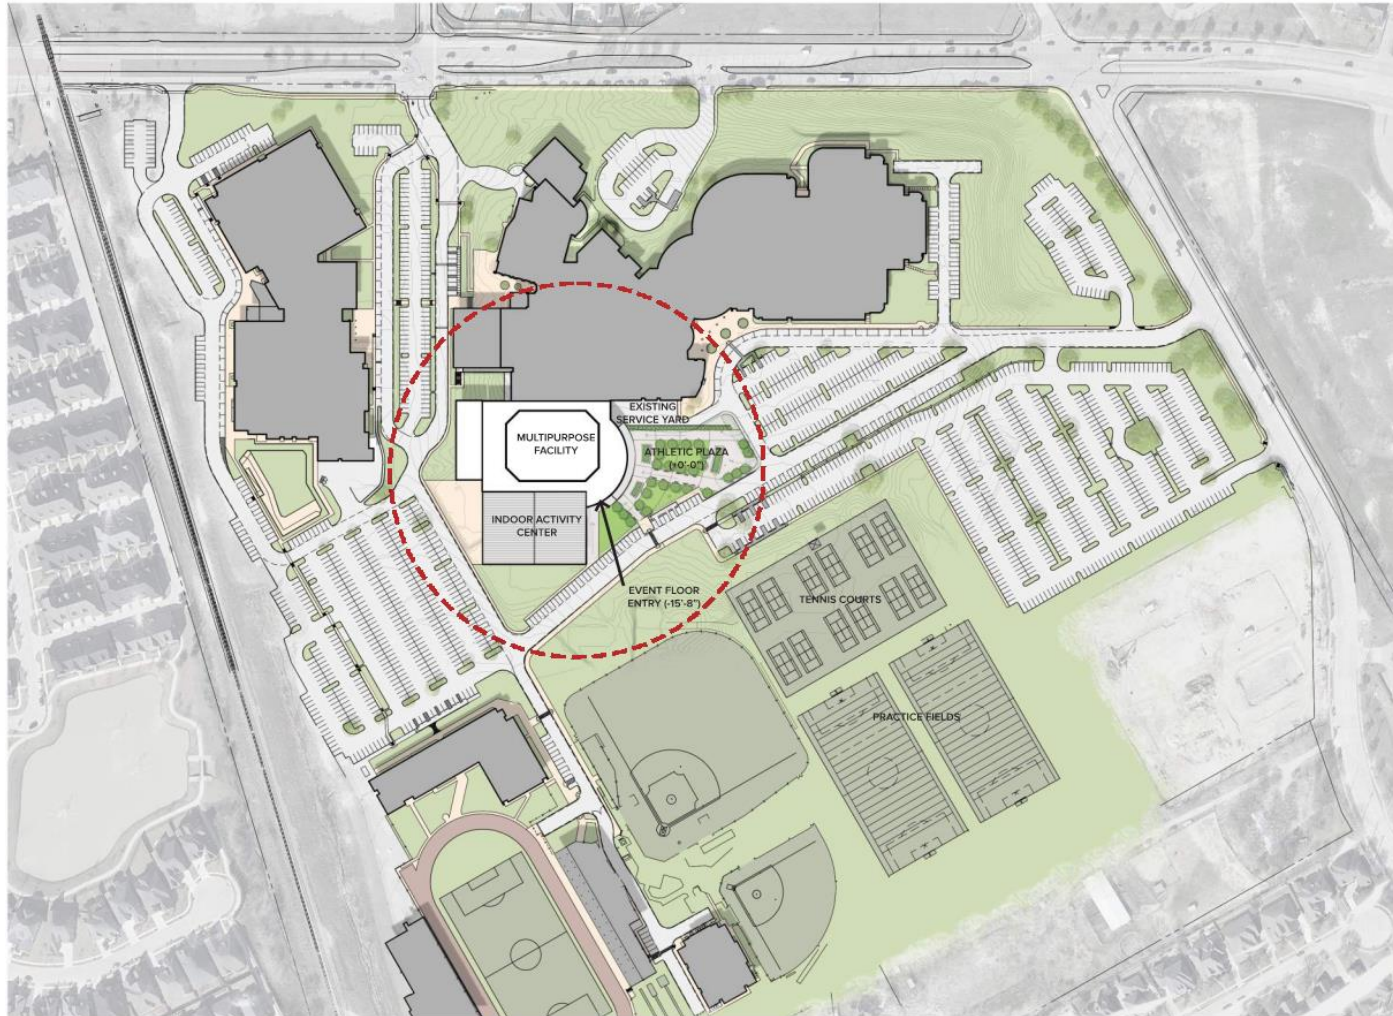

COLOR LEGEND	
	Pavement/Roads
	Sidewalks
	Grass
	Playing Fields
	Trees
	Detention Ponds
	Retention Ponds
	Track/Infields/Tennis
	Buildings
	Surrounding Property/Context

**Huckabee**

Hebron High School Multipurpose Facility & IAC




SITE PLAN



04

# HEBRON HS MULTI-PURPOSE/IAC



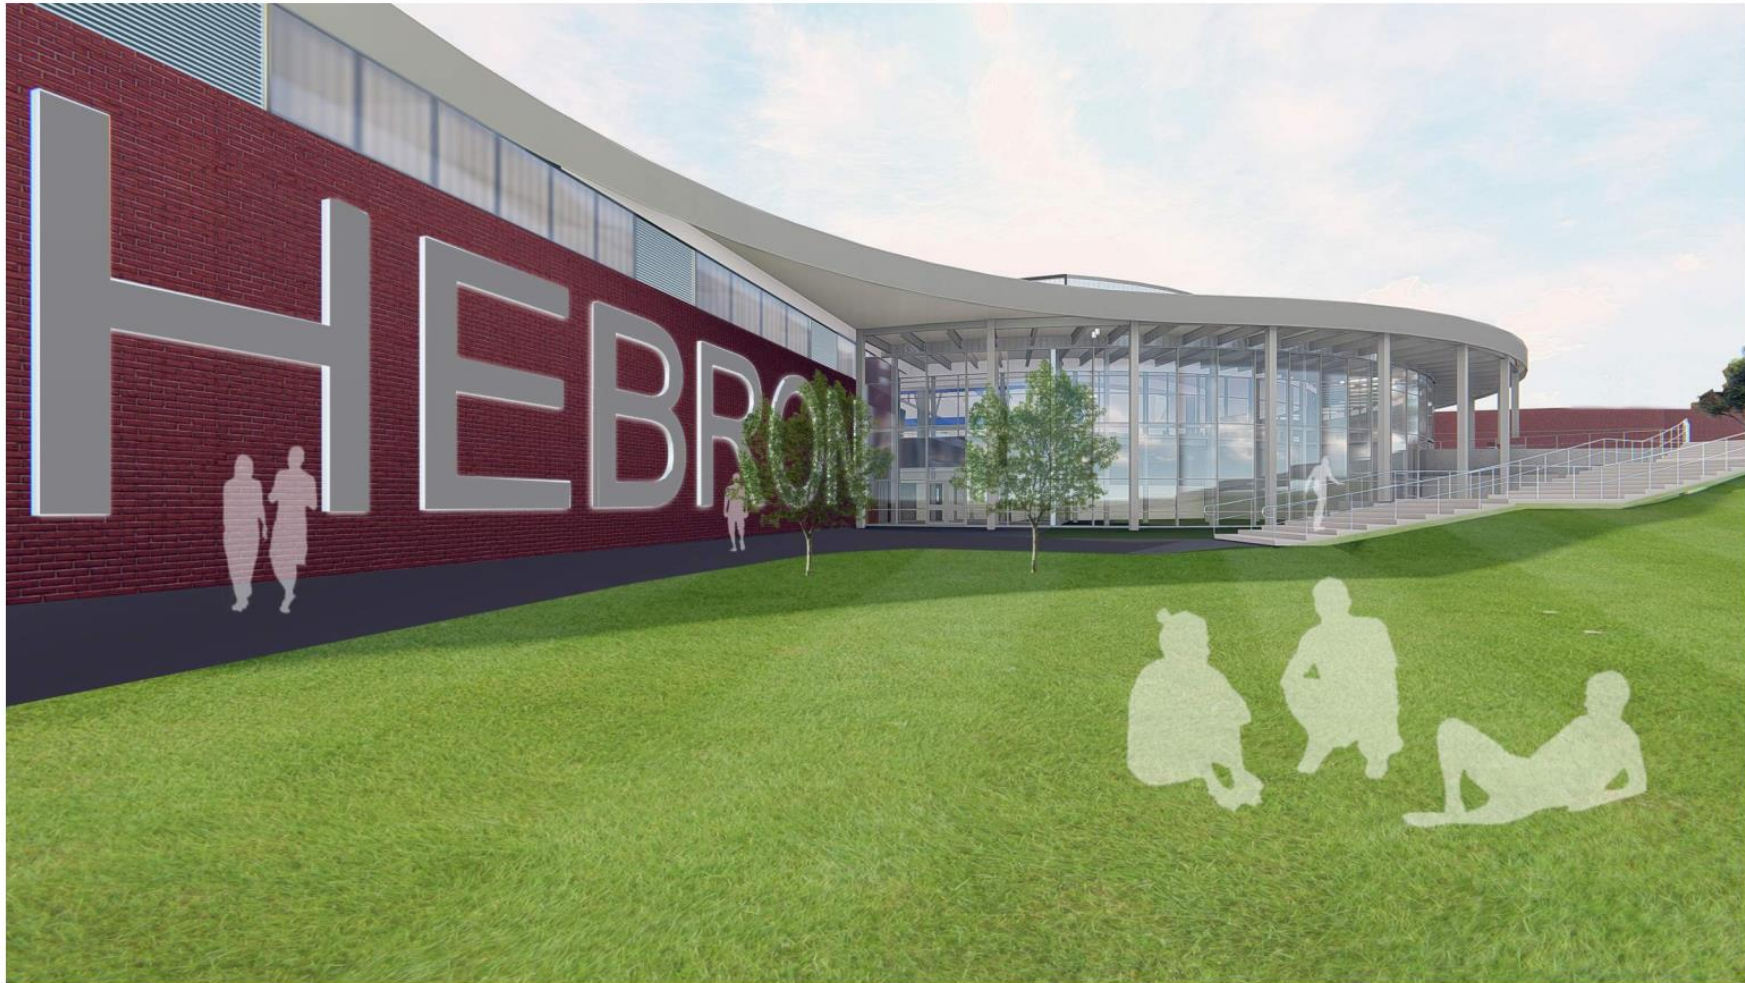

**Huckabee**

Hebron High School Multipurpose Facility & IAC

RENDERING - LOWER ENTRANCE

07

HEBRON HS MULTI-PURPOSE/IAC





**Huckabee**

Hebron High School Multipurpose Facility & IAC

RENDERING - CONCOURSE

07

# HEBRON HS MULTI-PURPOSE/IAC





**Huckabee**

Hebron High School Multipurpose Facility & IAC

RENDERING - COURT

07

# HEBRON HS MULTI-PURPOSE/IAC





**Huckabee**

Hebron High School Multipurpose Facility & IAC

RENDERING - WEIGHT ROOM

07

# HEBRON HS MULTI-PURPOSE/IAC



# LISDOLA RENOVATIONS







LISDOLA RENOVATIONS



# 20-YEAR REFRESH

- DEGAN ES 20-YEAR REFRESH: PRESENT TO BOARD FOR APPROVAL ON 2/11
- PARKWAY ES 20-YEAR REFRESH: PRESENT TO BOARD FOR APPROVAL ON 2/11
- TIMBERCREEK ES 20-YEAR REFRESH: PRESENT TO BOARD FOR APPROVAL ON 2/11
- VALLEY RIDGE ES 20-YEAR REFRESH AND STEM: PRESENT TO BOARD IN MARCH



# THE COLONY HS ENTRANCE








# THE COLONY HS ENTRANCE RENOVATION





# QUESTIONS?





# Lewisville ISD 2017 Safety and Security Bond Update

2/6/19







# 2017 Safety and Security Bond Update

- Enhanced lighting phase II approved during January Board Meeting
- Access control upgrades are currently in progress
- Security Cameras
  - Phase 1- 621 existing cameras replaced about 174 left for spring/summer 2019
  - Phase 2- 1,344 cameras added. Currently on punch lists and getting cameras onto the system
  - Phase 3- Campuses up for 20-year refreshes planned for summer 2019 We will be seeking Board approval this spring for this final phase













# 2017 Safety and Security Bond Update

- Security vestibules
  - District standard by floorplan to meet criteria
  - Elementary schools scheduled to be complete by fall 2019
- Communication and Network Access Completion
  - Replacement of phone system is complete (spring 2018)
  - Fiber project currently in engineering/city approval stage at Dixon (fall 2019)
  - Fiber project currently in design for Eastside Aquatic and LISDOLA (2019)



# Technology Plan Update

February 04, 2019



LEWISVILLE INDEPENDENT SCHOOL DISTRICT



# Technology Highlights - Infrastructure


- ✓ Installed new wireless system at 72 locations - nearly 6,000 new access points and over 400 new switches(I 1.2)
- ✓ Installed new VoIP phone system at 53 locations - over 4,600 new phones(I 1.3)
- ✓ Implemented district-wide 911 notification system(I 1.3)
- ✓ Completed cyber security upgrades - increased BitSight security rating score by 70 points(I 3.2)
- ✓ Implemented staff cyber security awareness training program(I 3.3)





# Technology Opportunities - Infrastructure

- ❑ Design secondary datacenter(I 2.2)
- ❑ Design first stages of redundant mesh Wide Area Network(I 2.3)
- ❑ Complete Datacenter Storage and Network Upgrades(I 2.4)
- ❑ Perform cyber security testing and evaluation by outside firm(I 3.2)





# Technology Highlights- Technology Resources

- ✓ Residual Value Project- more value than projected (TR 1.1)
- ✓ Microsoft Agreement (TR 1.2)
- ✓ Device Deployment (TR 1.1)
  - Completed Device Evaluation & Device Refresh Plan
  - Implemented Year One on time and under budget
    - Deployed 48,674 Devices (Instructional and Program Specific)
      - 29,487 New, 15,971 Repurposed, 3,216 Program Specific
- ✓ Device Management Selection and Implementation (TR 2.1)
- ✓ Improved processes for inventory management (TR 2.1)





# Technology Opportunities -Technology Resources



- **Complete Year 2 Bond Projects** (TR 1.1)
    - 1:X Program Deployment for 2019-2020 Grades 7, 8, 9
    - Classroom Set iPad Deployment for Grades PK-3
    - Complete Districtwide Zone Printing Project
  - **Residual Value** (TR 1.1)
    - Develop and execute plan for districtwide end of life Apple products.
  - **Focus on Continual Service Improvement Process** (TR 3.2)





**Thank You and  
Questions**

